UptimeEquip
Innovative Maintenance Support Program

SelectEquip
Flexible Innovative Packaging Systems

GENERAL SERVICE REPORT

Customer:	Coles ROAA	**Date:**	18th January
Site Address:	54 Templar Rd, Erskine Park NSW 2759	**Site Contact:**	Alan Villa
		Phone:	0410 556 153
Customer PO #:		**Internal Job #:**	4264

Subject: XT500 film trial Platformer

Equipment Type:	Serial Number:	Customer Line # (if applicable):
Trave 590	A17A-11614	Line 4
Platformer	A17A-11614	Line 4

Equipment condition:

Work Performed:

Thursday 18th

- *Called in to help support Sealed Air XT500L bottom web on Platformer.*
- *Before starting we needed to remove the lower P&P plate to replace a few damaged dampers.*
- *Created a new recipe call "Large DOT Cryovac " with a few changes to recipe*
- *We could not run the film below 140C before the film sheets start dropping off the Diffuser.*
- *We could not run the film about 145C before we start affecting the trays top barrier.*
- *We have a very fine line between temperature too low or too high.*
- *The presentation of the trays are better with the edges forming okay, this is an improvement of the previous trays in presentation but my only concern is the temperature and tray barrier*
- *The P&P temperature was increase to 170C*
- *We delayed the lower vacuum mould to 0.1sec to try prevent stress during forming.*

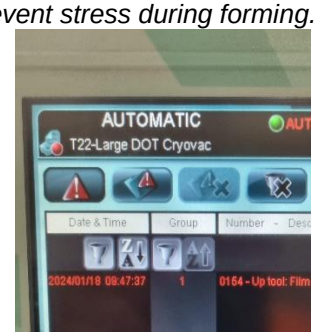

- *The Trave 590 recipe needed some tuning to run the new trays*
- *We found they disabled the auto-heat for shuttle which we have reintroduced.*
- *We improved the compensation by making it more aggressive so the film does not cool down during the cycle.*
- *Presentation of the product looks better and seems to be running okay.*
- *Note the performance will need to monitor over time on the 11x9 trays.*
- *We replaced a few of the suction cups on 9x8 P&L plate*
- *We replaced a few of the dampers*

UptimeEquip
Innovative Maintenance Support Program

SelectEquip
Flexible Innovative Packaging Systems

GENERAL SERVICE REPORT

TECHNICIAN HOURS Marc Ashford Thursday 18th					
Time	**Start**	**Finish**		**Start**	**Finish**
Travel To Site:	04:00	05:00			
Onsite:	05:00	11:00			
Travel From Site:	11:00	11:30			

REPORT SIGN OFF			
	Print Name:	**Signature:**	**Date:**
Customer:		X	18th January
Technician:	Marc Ashford		

Select Equip
7 Gatwick Road Bayswater North
Victoria 3153 Australia
Phone +61 (3) 8720 8400

Trading as Select Equip
Select Packaging Systems Pty Ltd ABN 59 087 731 520
spares@selectequip.com.au www.selectequip.com.au
